


ZEUS Shutdown Plans

No news is good news

W.Zeuner

Removal tool for FDET is ready for use

- Overload test passed (~ 1t instead of 700 KG)
- Shown to D5
 - Prepare some add. Documentation

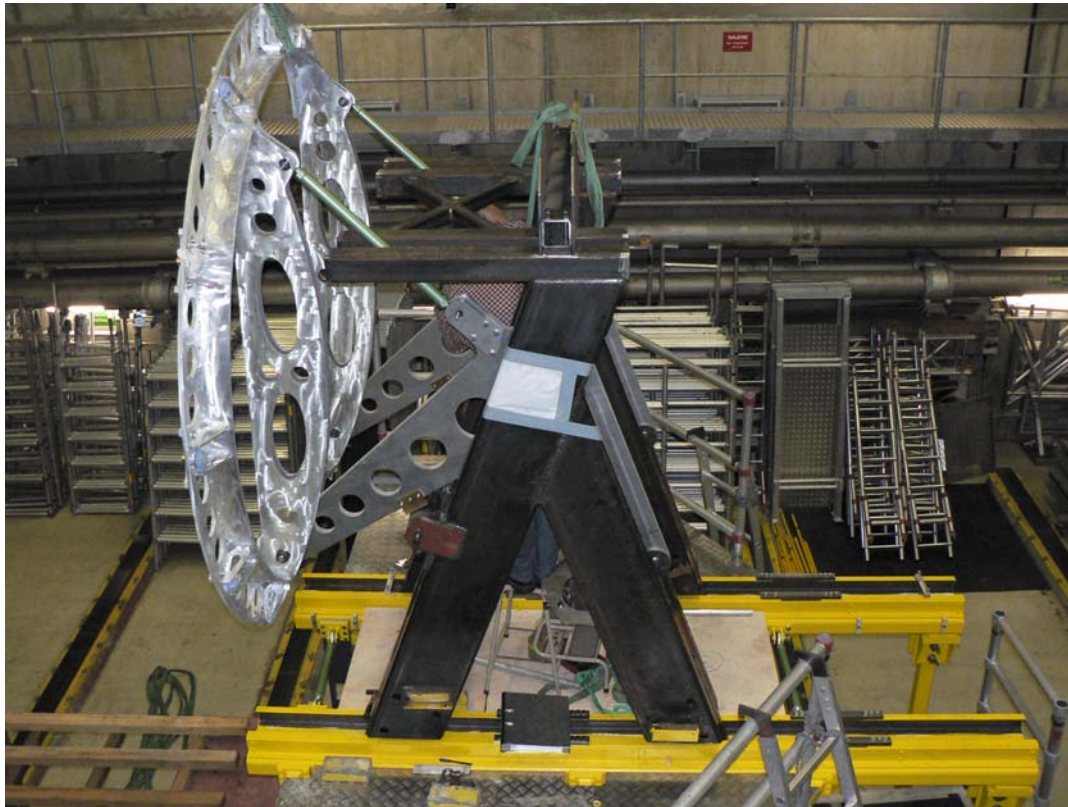

Support for GO ready for use

- Deformation well within limits
1000 N sideward ~ 0.45mm



Cooling of the FDET Area

- Cooling pipes for the FDET region are ready
waiting for transport from Bonn to HH
- Cooling machine has been delivered

FDET REPAIR IS PREPARED

Repair of other Components

CAL, HES, BAC, B/RMUON, SRTD, CFLT

All fits into the schedule

Preparation is on schedule

ZEUS is ready for the shutdown
